



Edgewater Expansion Design

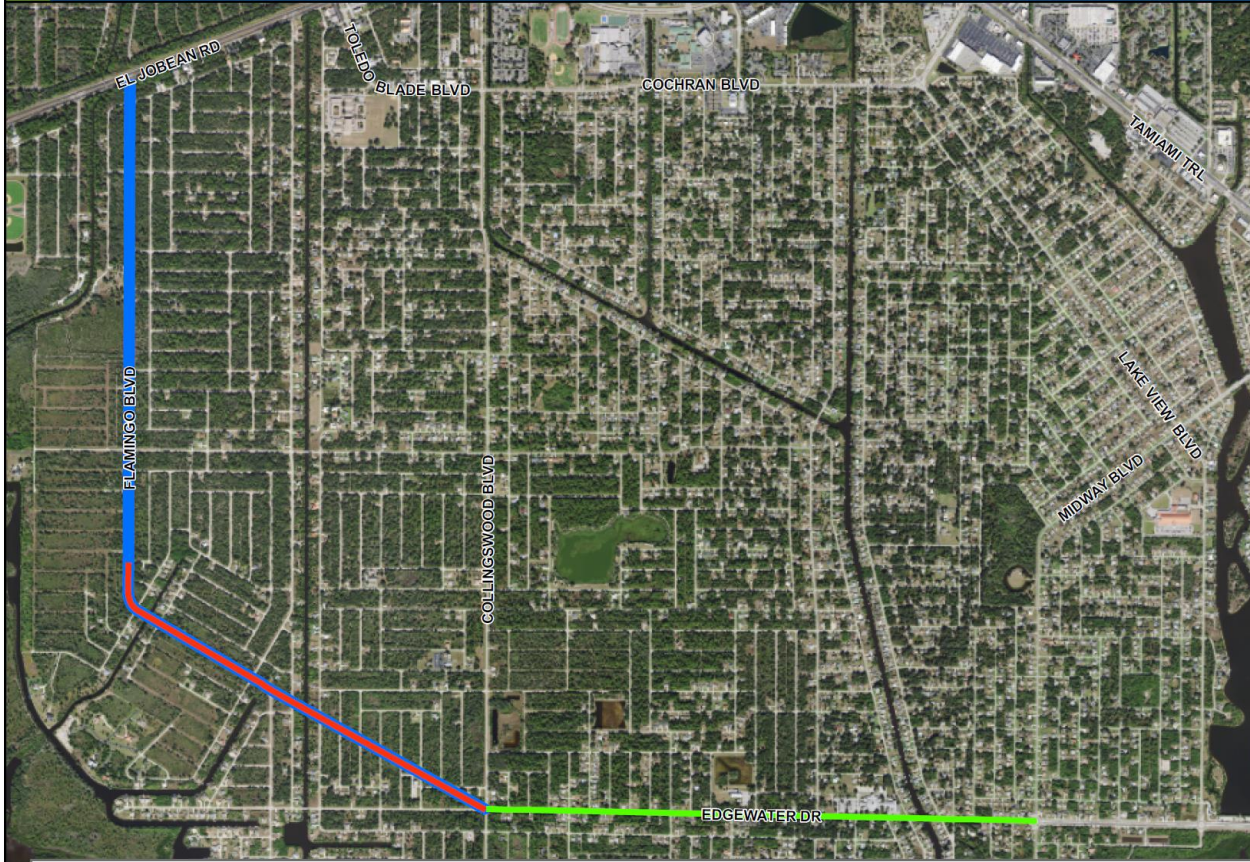

- Design Edgewater Corridor Phases 3-5
 - Design Contract w/ Johnson Engineering \$5,068,415
 - 100% plans expected in Summer 2025
 - Land acquisition is ongoing

Completed 2020 Sidewalks

- Marathon Boulevard
 - Gasparilla Road to the Cape Haze Pioneer Trail
 - Design \$43,295
 - Construction \$355,112
- Sunset Boulevard
 - Bermont Road to South Fairway Drive
 - Design \$38,395
 - Construction \$444,378

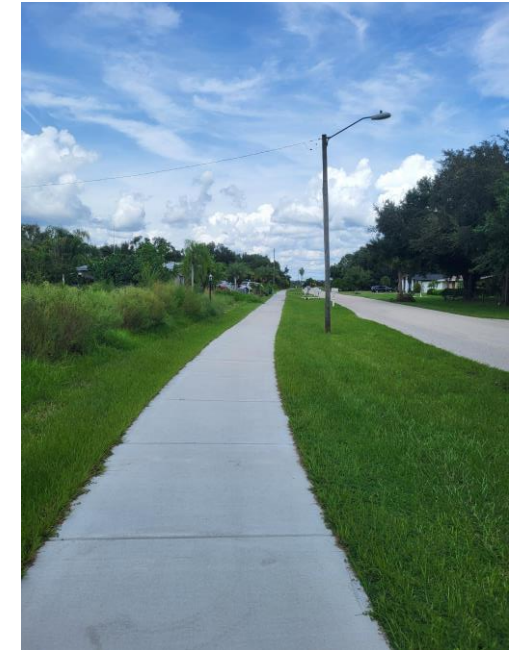

Fruitland Boulevard/ Avenue of the Americas Sidewalk



- Fruitland Boulevard – Gulfstream Boulevard to Winchester Boulevard
- Avenue of the Americas – Winchester Boulevard to San Casa Drive
- Construction – 95% complete
- Scheduled to be complete May 18, 2025
- Design \$170,960
- Construction \$1,800,567


Quesada Boulevard Sidewalk

- Cochran Boulevard to Forrest Nelson Boulevard
 - Includes pedestrian facilities at Forrest Nelson Boulevard
 - Scheduled to be completed May 2025
- Design \$133,681
- Construction \$969,390




Rampart Boulevard Sidewalk

- Kings Highway to Rio De Janeiro
 - MSBU continuing sidewalk to Navigator Road
 - Completing as one project for cost savings
 - Preliminary design phase/coordination with FDOT on overpass
 - 30% plans due April 2025
- Design \$343,253

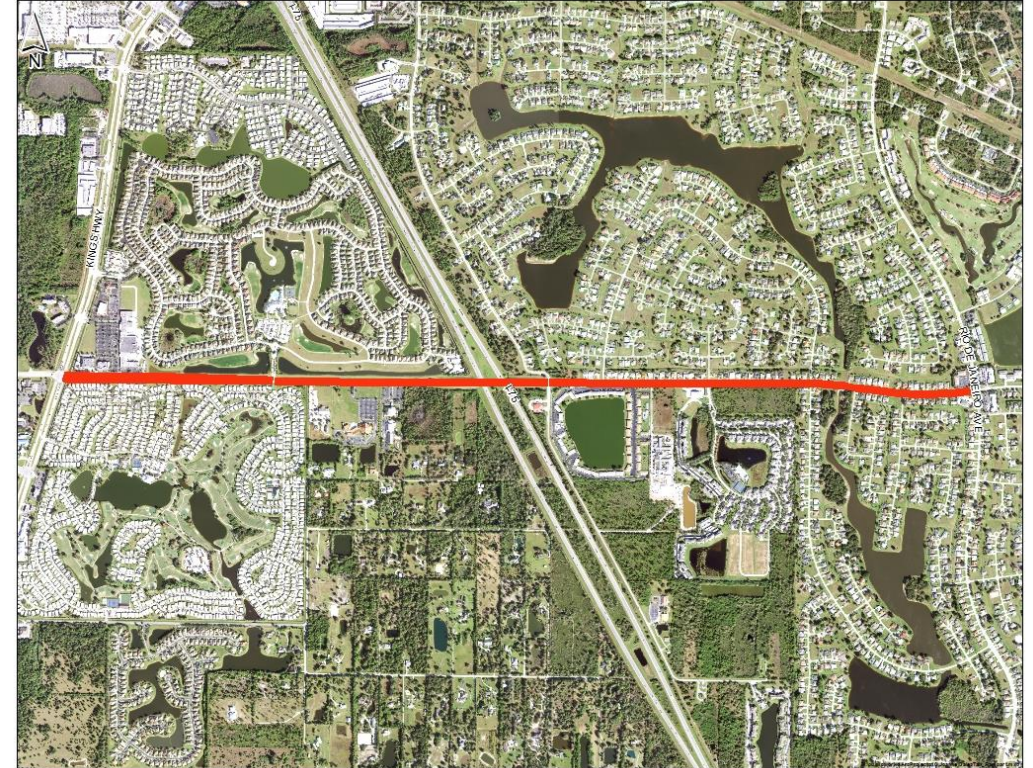

Caring Way and Brinson Avenue Sidewalk

- Caring Way - Olean to Gertrude
- Brinson Ave – Caring Way to Harbor Blvd
- Preliminary design phase
- 60% plans due June 2025
- Design \$181,080

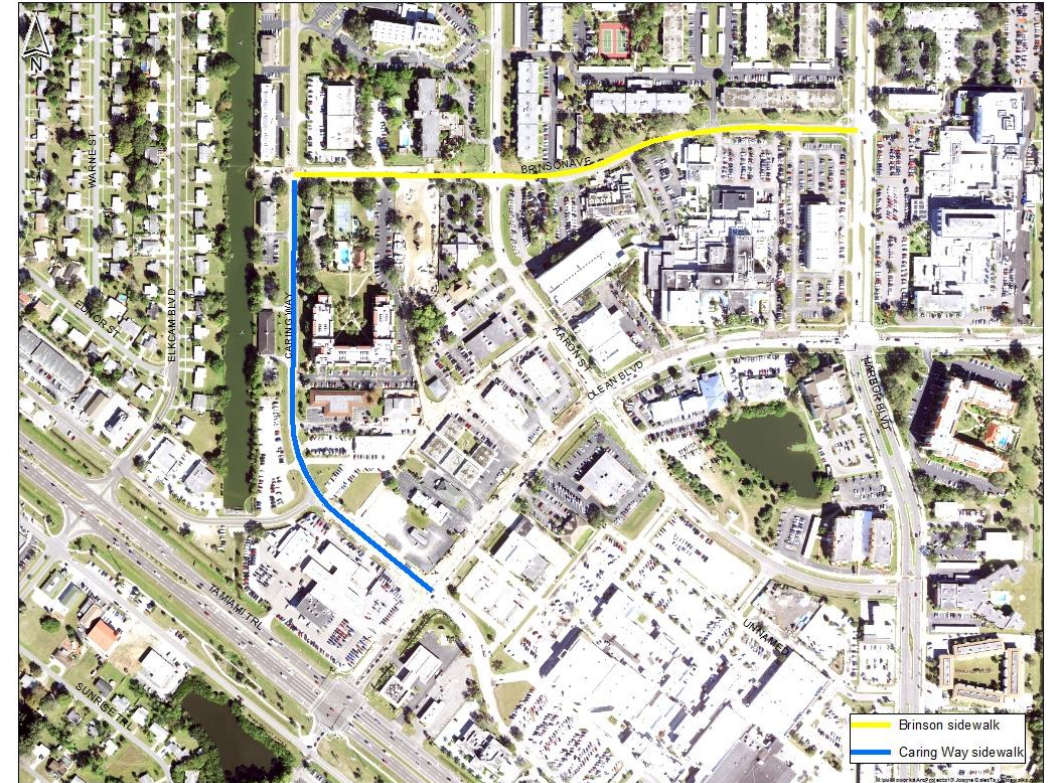

Atwater Street Sidewalk

- Veterans Blvd to County line
- 90% plans due May 2025
- Design \$87,555



Cleveland Avenue Sidewalk

- From US17 to Riverside Drive
- 90% plans received in March 2025 under review by staff
- Coordination with the railroad has started
- Design \$62,010



Airport Road Sidewalk

- From Florida Southwestern State College driveway to Piper Road
- Staff is looking at estimates and available funding before starting the design process.

