AMENDMENT #1 TO CONTRACT NO. 2021000470 BETWEEN CHARLOTTE COUNTY

and WHARTON-SMITH, INC.

for

CONSTRUCTION MANAGER AT RISK - SHERIFF'S ADMINISTRATION/HARDENED 911 FACILITY

THIS AMENDMENT #1 to Contract No. 2021000470 (the "Amendment") is made and entered into by and between CHARLOTTE COUNTY, a political subdivision of the State of Florida, 18500 Murdock Circle, Port Charlotte, Florida 33948-1094 (the "County"), and WHARTON-SMITH, INC., 4912 W. LaSalle Street, Tampa, Florida 33607 (the "Construction Manager").

RECITALS

WHEREAS, the County and the Construction Manager entered into Contract No. 2021000470 (the "Agreement") on or about December 2, 2021, to engage the Construction Manager for preconstruction and construction services for the Sheriff's Administration/Hardened 911 Facility in Charlotte County, Florida (the "Project"); and

WHEREAS, pursuant to the terms of the Agreement, the Project is to be completed in two phases, Phase I – Pre-Construction Services, and Phase II – Construction Services; and

WHEREAS, Phase I of the Project - Pre-Construction Services - is complete; and

WHEREAS, the Guaranteed Maximum Price ("GMP") for Phase II of the Project has been submitted by the Construction Manager, and pursuant to the Agreement, the GMP shall be made a part of the Agreement by an amendment to the Agreement; and

WHEREAS, the parties now wish to amend the Agreement to provide for the GMP, to provide for a time for completion, to provide certain additional terms and conditions and to provide for Liquidated Damages in the event the Construction Manager fails to achieve substantial completion as set forth herein.

NOW, THEREFORE, in consideration of the mutual covenants contained herein, the County and the Construction Manager agree as set forth below:

ARTICLE I GUARANTEED MAXIMUM PRICE

- 1.1. The GMP Summary, Bid Tabulations, General Conditions, Clarifications and Schedule & Site Logistics, submitted by Construction Manager, are attached hereto as **Exhibit A**, Guaranteed Maximum Price, and **Exhibit A** is specifically incorporated into and made a part of the Agreement.
- 1.2. In accordance with the terms of the Agreement and **Exhibit A** attached, the parties agree that the Guaranteed Maximum Price for the Project is Thirty-Seven Million Two Hundred Fifty-One Thousand Three Hundred Eighty-Six Dollars and No Cents (\$37,251,386.00).

1.3. All applications for, and terms of, payment for Phase II of the Project shall be in accordance with Article 6 of the Agreement.

ARTICLE II LIQUIDATED DAMAGES

- 2.1. Pursuant to the GMP Schedule, **Exhibit A**, attached, construction services shall be completed on or before January 6, 2026.
- 2.2. Pursuant to Article 11.4 of the Contract, Liquidated Damages are established at Five Hundred Dollars and No Cents (\$500.00) per day.

ARTICLE III MISCELLANEOUS

- 3.1. The effective date of this Amendment is the date on which it is signed by both parties.
- 3.2. Any terms used in this Amendment shall have the same meanings and definitions as they have in the Agreement.
- 3.3. All other provisions of the Agreement not in conflict with this Amendment shall remain in full force and effect.


[REMAINDER OF PAGE INTENTIONALLY LEFT BLANK]

IN WITNESS WHEREOF, the parties hereto have entered into this Amendment on the dates indicated below.

WITNESS:	WHARTON-SMITH, INC.
Signed By:	Signed by:
Print Name:	Print Name:
Date:	Title:
	Date:
	BOARD OF COUNTY COMMISSIONERS OF CHARLOTTE COUNTY, FLORIDA
ATTEST: Roger D. Eaton, Clerk of the Circuit Court and Ex-Officio Clerk to the Board of County Commissioners	By: William G. Truex, Chairman
By: Deputy Clerk	Date:
	APPROVED AS TO FORM AND LEGAL SUFFICIENCY:
	Janette S. Knowlton, County Attorney LR24-0232

Exhibit List:

 $\hbox{Exhibit A-GMP Summary, B$_{\underline{i}}$ d Tabulations, General Conditions, Clarifications and Schedule \& Site Logistics \\$



Wharton-Smith, Inc.

Table of Contents

Tab 1 – Executive Summary

Tab 2 – GMP Summary

Tab 3 – Bid Tabulations

Tab 4 – General Conditions

Tab 5 – Clarifications

Tab 6 – Schedule & Site Logistics



Tab 1 – Executive Summary







EXECUTIVE SUMMARY

Wharton-Smith is pleased to submit our Guaranteed Maximum Price (GMP) for Construction Services on the Charlotte County Sheriff's Administration/Hardened 911 Facility project. We have assembled a highly experienced team of professionals for this project and are committed to ensuring that our team meets all the requirements and expectations for Charlotte County Public Schools.

The GMP is being presented at \$37,251,386

With respect to the remainder of the GMP assembly, we have provided the following:

- All subcontracts over the amount of \$100,000 are bonded which is included in the GMP.
- A Clarification and Qualifications document was prepared to clarify items that may not have been addressed or may not be clear in the documents. The Clarifications are only offered to resolve any confusion and to allow the construction phase to progress as smoothly as possible.
- Finally, a construction schedule is presented, consistent with our understanding of the time frames involved. The Schedule is detailed showing durations, Critical Path and assumptions made. This schedule will provide the basis for managing time as well as individual subcontractor's impact.

Putting together all these documents will provide a complete understanding of our proposal to construct the project. We look forward to working with you on this important project.

Respectfully,

Juanmiguel Gorut Preconstruction Executive Wharton-Smith, Inc.

Tab 2 – GMP Summary





Sheriff's Administration/Hardened 911 Facility

Charlotte County

ESTIMATING WORKSHEET SUMMARY

Building Area

64,735 SF

2/15/2024

LINE	SPEC	DESCRIPTION		\$/SF		TOTAL	
1		Direct Costs					
2							
4	030000	Cast In Place Concrete	\$	34.49		2,232,973	
5	031000	Pre-Cast Hollow Core Planks	\$	3.54		228,990	
6	050000	Structural Steel	\$	24.58	committee, despite any other factors despited	1,591,200	
7	052000	Railings	\$	1.58	************	1,391,200	
8	062000	Finish Carpentry	\$	1.44		92,959	
9	071000	Damproofing & Waterproofing		1.44		95,680	
10	070000	Spray Fireproofing	\$	3.09	***************************************		Allowance
11	074000	Metal Cladding	\$				Allowance
				5.41			Allowance
12	075000	Roofing	\$	12.63		817,550	A 11
13	081000	Doors, Frames & Hardware	\$	12.43			Allowance
14	083000	Specialty Doors	\$	1.30		84,224	
15	085000	Glass & Glazing	\$	15.85		1,025,846	ļ
16	092000	Drywall, Framing & Insulation	\$	25.60	*************	1,657,409	ļ
17	095000	Acoustcial Specialties	. \$	6.80		439,969	ļ
18	096000	Flooring & Tile	\$	14.42		933,185	
19	099100	Painting	\$	6.35		411,086	
20	100000	Specialties	\$	2.55		164,817	
21	105000	Identifying Devices	\$	0.97		62,853	
22	108000	Protective Covers	\$	2.06	****	133,511	
23	124000	Window Treatment Blinds	\$	1,36		87,957	
24	140000	Elevator	\$	3.67		237,660	
25	210000	Fire Sprinklers	\$	6.36		. 411,844	
26	220000	Plumbing	\$	16.14		1,045,141	
27	230000	Heating, Ventilation & Air Conditioning	\$.	69.23		4,481,625	
28	260000	Electrical	\$	88.56		5,732,641	
29	270000	Low Voltage	\$	20.02		1,295,782	T
30	280000	Video Wall & Consoles	\$	27.17		1,758,866	
31	310000	Site Earthwork, Utilities & Paving	\$	36.41		2,356,885	1
32	329300	Landscaping & Irrigation	. \$	3.44		222,673	
33		TOTAL DIRECT COSTS	\$	448.90		29,059,782	
34							1
35		Indirect Costs					
36		General Conditions	\$	39.81	***************************************	2,577,151	
37		General Requirements	\$	11.53		746,503	†
38		BIM Services	· \$	0.58	0.10%	37,251	
39		IT Software	\$	1,21	0.21%	78,228	·
40	······································	Design Contingency	\$		0.00%		1
41		Escalation Contingency	\$		0.00%	-	
42		General Liability Insurance	\$	4.03	0.70%	260,760	·
43		Builder's Risk Insurance	. \$	7.89	1.37%	510,567	
44		Permits	\$	7.89	0.00%	510,507	
45		P&P Bond	\$	3.08	0.00%	199,107	,1
					0.53%		
46		SUBTOTAL	\$	517.02		33,469,350	
47				25.65	E 000'	+	
48		Construction Contingency	\$	25.85	5.00%	1,673,467	
49		SUBTOTAL	\$	542.87		35,142,817	
50							
51		Fee	\$	32.57	6.00%	2,108,569	THE PERSON NAMED IN COLUMN 2 IS NOT THE OWNER.
52		Guaranteed Maximum Price	\$	575.44		37,251,386	

Tab 3 – Clarifications



Thursday, February 1, 2024





The Project

The Charlotte County Sheriff's Administration Center project involves the construction of a new 62,441 SF 2-story building to include the Sheriff Office's Support Headquarters. The building will not be constructed as an E.H.P.A or storm shelter building. The second floor will contain approximately 12,000 SF of access flooring in the Intelligence/RTIC division analysis rooms, offices, Dispatch / Call Taker space, and training rooms. The first floor will have a community room that can hold up to 250 people. A vehicle maintenance bay is attached to the east side of the main building - servicing up to (4) vehicles. Building's construction is Type II B and will be fully sprinkled.

Documents

Please see Documents log attached herein.

Schedule

- Please see Schedule attached hererin.
- A GMP approval date for the project is assumed to be March 12th 2024
- Should the project be delayed beyond the start date set above, there could be an impact on final project cost.

- The GMP contains a construction contingency to allow for unforeseen events, errors and omissions
- Any increases related to market escalations discovered during procurement of long-lead items and packages shall be funded via construction contingency.

GC, GR and Staffing

■ Upon execution of the GMP, the general conditions labor and general requirements will convert to lump sum and be billed out as a fixed amount on a monthly basis divisible by the total duration of the project shown per the contract schedule. The labor rates are then auditable only to confirm the total hours used on the project, not to the composition thereof.

Insurances and Bonding

- For all subcontractors with a contract in the amount of \$100,000 or more bonding cost has been included in the estimate
- Payment & Performance Bond included
- Standard General Liability Commercial Contractor Insurance coverage included
- Builder's Risk Insurance was included

<u>Fee</u>

As negotiated

Owner Costs

To eliminate confusion caused by duplication and/or omissions, the following costs are assumed to be held by the Owner:

- Impact fees and other fees charged by the County, SWFWMD, any State or Federal agencies
- Utility meters and metering devices normally provided by the Utility Company
- Electric / Utility costs of any kind
- Design and engineering costs
- We have assumed that the cost of temporary electric would be supplied be the Owner by virtue of the systems on the existing
- Hazardous material testing or demolition / removal (asbestos, mold, lead paint, etc.)

Thursday, February 1, 2024 Clarifications



Direct Costs

Concrete

As shown

Metals and Railings

■ As shown

<u>Carpentry</u>

Plastic Laminate labeled PL-3 is considered to be PL-1 per RFI Response #1-001

Spray-on Fireproofing

Spray-on fire proofing is included as an allowance; construction is noted as Type II B which doesn't require it, but partition wall details indicate areas with it called out.

Roofing/Thermal Protection

Factory Mutual requirements are included; however, their involvement with inspections is excluded from this GMP

Doors, Frames & Hardware

Doors, frames and hardware package is considered an allowance as the door hardware schedule remains to be coordinated with floor plan designations and specifications. Hardware package reconciliation may result in revisions to door leaf and frame prep.

Overhead Doors

■ Doors based on Clopay Model 3722-W8 & 522

Windows and Glass

- Non-thermal frames are included.
- (3) days of air / water testing are included.
- YKK First Choice panic exit devices included to meet Missile Level E rating at all storefront openings
- SF-1 & SF-2 included as curtainwall system due to height limitations shown exceeding storefront impact rating criteria; break metal assumed for sections between clear glass areas as shown however to meet missile impact rating spandrel glazing will be required. Any cost impacts for spandrel glazing to replace the noted break metal shall be funded through project contingency.
- Exterior HM door narrow vision lites have not been tested with missile level E impact requirements; all openings shown with this
 detail must be replaced with flush HM doors. Therefore these vision lites at these conditions are excluded.

Finishes

- Technowood Veneer system is included as an allowance due to the local certified distributor being non-responsive. Pricing to be reconciled at a later date.
- Air barrier at Technowood system is excluded, none, shown; if required, shall be funded from allowance noted.
- WD-1 and W-1 are the same wood paneling product described in specification section 06 42 00 per RFI Response #1-003
- Exterior metal framing to be G90; interior to be G60
- Sound walls to have STC-47 rating
- Level 4 finish is included

Canopies

- Canopies based on Architectural Metals proprietary system to include (3) separate canopies fastened together with visible splices where canopies meet.
- Arm braces shall be 2" sq. tubing.
- Finish shall be AAMA 2604 high performance organic coating selected from RAL classic K-7 color chart.

Thursday, February 1, 2024

Clarifications



FF&E / Specialties

- Mobile High Density Storage Shelving in Specification Section 10 56 26 is by Sheriff's Office and is excluded per RFI Response #2-011
- Defibrillators, Cabinets and Accessories are not required per correspondence with the owner and RFI Response #3-026. These items are excluded

Elevators

Based on Otis Hydrofit Elevator System

Fire Sprinklers

As shown

Plumbing

Air compressor to be provided by the Owner per P101B in lieu of architectural equipment schedules indicating contractor supply.

<u>Mechanical</u>

Keynote 3 on Drawing Sheet MD010 is unneeded as the generator has not been relocated per RFI Responses #2-012, #2-013,
 #2-014, #2-015 & #2-016. Relocation of the existing generator is excluded from this proposal

Electrical

- Lightning protection tower is assumed by the Owner Utility company; therefore it is excluded from the bid
- Primary conduits and primary transformer are excluded by Owner
- Panels CLSH1 and LSH2 are priced as 125A panels ILO 60A panels per RFI Responses #1-004 & #1-005
- Panels RP2A and RP2B are priced as 225A panels ILO 150A panels per RFI Response #1-006
- Panels LCP1 and LCP2 have been removed per RFI Response #1-007
- Keynote 5 on Drawing Sheet E402 is to be disregarded per RFI Response #2-018. Overhead buses are fed from 125A breaker in panels UPS1 & UPS2

Low Voltage

- RTIC Video Wall proposed as LCD
- Security, CCTV and Access Controls are included as an allowance.

Site

Proposed 12" Watermain Tap & Valve on Sheet C-15 has been removed. No work in this area per RFI Response #2-010

Landscaping & Irrigation

- Water source assumes point of connection within proposed new scope of work for irrigation tie-ins; if additional mainline install is required to make point of connection then it must be funded via contingency.
- Assumes installation of a new irrigation controller.


Tab 4 – Schedule & Site Logistics



-,	CHARLOTTE COUNTY				Charlotte County Sh	harlotte County Sheriff's Admin/911 GMP	Data De Project ID: 2'	Data Date: 01-Feb-24 Project ID: 21-146-1-30-24
Activity ID	Activity Name	Oria	Start	Finish	2024	24	2025	2026
,		Dur			Feb Mar Apr May Jun	Jul Aug Sep Oct Nov Dec Jan Feb Mar Apr May	Jun Jul Aug Sep Oct Nov Dec Jan	Feb Mar
Charlotte Cou	Charlotte County Sheriff's Admin/911 GMP	504	01-Feb-24	06-Jan-26				
MILESTONES	Ŋ	459	12-Mar-24	06-Jan-26				
A5030	Board Meeting	0	12-Mar-24*		◆ Board Meeting			
A5100	NTP	0	04-Apr-24		◆ NTP			
A5220	Mobilize	0	19-Jul-24			◆ Mobilize		
A5200	Substantial Completion	0		11-Dec-25			◆ Substantia	Substantial Completion
A5210	Final Completion	٥		06-Jan-26			₩ •	Final Completion
PRECONSTRUCTION	RUCTION	443	01-Feb-24	13-0ct-25				
A5040	GMP Submission	-	01-Feb-24	01-Feb-24	.=			
A5010	GMP Board Approval	ω	12-Mar-24	18-Mar-24	GMP Board Approval			-
A5020	Prime Contract Amendment Ratify & Execute	12	19-Mar-24	03-Apr-24	Prime Contract Amendment Ratify & Execute	Iment Ratify & Execute		
A5090	NTP	-	04-Apr-24	04-Apr-24	den e			
Permitting		114	01-Feb-24	12-Jul-24				
A5050	Building Permit	63	01-Feb-24	30-Apr-24	Building Permit			
A5060	Site Permitting	63	01-Feb-24	30-Apr-24	Site Permitting			
A5070	R.O.W. Permit	45	09-May-24	12-Jul-24		■ R.Ö.W. Permit		
A5080	Utility Permitting	45	09-May-24	12-Jul-24		Utility Permitting		
Procurement	-	410	19-Mar-24	13-Oct-25				
A5250	Transformer Procure & Install	150	19-Mar-24	14-Oct-24		Transformer Procure & Install		
A5110	Subcontract Agreements Execute	25	04-Apr-24	08-May-24	Subcontract	Subcontract Agreements Execute		
A5120	Long Lead Submittals	35	18-Apr-24	06-Jun-24	Long	Long Lead Submittas		
A5130	Purchase Agreements	20	07-Jun-24	05-Jul-24		■ Purchase Agreements		
A5140	Generator Procure & Deliver	320	08-Jul-24	13-Oct-25			Generator Procure & Delive	, ei
A5150	AHU Procure & Deliver	245	08~Jul-24	26-Jun-25			AHU Procure & Deliver	
A5160	Electrical Panels Procure & Deliver	155	08-Jul-24	19-Feb-25		Electrical Panek Procure & Deliver	& Deliver	
A5170	Chillers Procure & Deliver	190	08-Jul-24	28-Mar-25		Chillers Procure & Deliver	& Deliver	
A5180	Formliner Procure & Deliver	25	08-Jul-24	09-Aug-24		Formliner Procure & Deliver		
A5190	Storefront & Windows Procure & Deliver	120	08-Jul-24	20-Dec-24		Storefront & Windows Procure & Deliver		
A5230	Access Floor	20	08-Jul-24	13-Sep-24		Access Floor		
A5240	Main Swithcgear Procure & Deliver	240	08-Jul-24	06-Jun-25			■ Main Swithogear Procure & Deliver	
Construction		332	19-Jul-24	27-0d-25				
Site Work		250	19-Jul-24	03-Jul-25				
SI-90	Mobilize	12	19-Jul-24	05-Aug-24		Mobilize		
SI-95	SWPPP	۵	23-Jul-24	01-Aug-24		dådMS		
SI-150	Building Pad	£	02-Aug-24	16-Aug-24		Building Pad		
SI-140	Storm System	15	31-Dec-24	20-Jan-25		Storm System		
SI-130	WM & FM Pipe/Test/Chlorinate	35	21-Jan-25	10-Mar-25		WM & FM Pipe/Test/Chlorinate	Chlorinate	
SI-160	Sugrade & Base	18	11-Mar-25	03-Apr-25		Sugrade & Base	as as	
SI-220	Directional Bore & Tie in	12	11-Mar-25	26-Mar-25		Directional Bore & Tie in	& Te in	
SI-180	Sidewalks	9	04-Apr-25	25-Apr-25		Sidewalks	S	
				-				
Actual Work Remaining Work	Critical Remaining Work ◆ Milestone					Page 1 of 3 Data Date: 01-Feb-24 TASK filter. All Activities		
				-				

		17 17 17	1		2025 2026	2026
Activity 10	2	Activity inditie	Dur		Feb Mar Apr May Jun Jul Aug Sep Oct Nov Dec Jan Feb Mar Apr May Jun Jul Aug Sep Oct Nov Dec Jan Feb Mar	Н
	SI-170	Paving	6 28-Apr-25	5 05-May-25	Pav	
	SI-190	Stripping & Signage	6 13-May-25			
	SI-200	Final Grading	6 21-May-25	5 28-May-25	Ē.	
1000	SI-210	Fending & Gates		_		
- T. C.	SI-230	Landscape	12 18-Jun-25		- Landscape	
	Building					
-	Structure & Envelope	Envelope		-		
*	BS-270	Elevator Pit Foundations & Walls				
	BS-140	Building Foundations				
	BS-150	MEP Slab Rough-In	16 17-Sep-24			
	BS-160	Casting Beds	8 09-Oct-24	18-Oct-24	Casting Beds	
*****	BS-170	S.O.G. Form/Reinforce/Pour	10 09-Oct-24	_	S.O.O.	
	BS-190	Form & Pour Panels	16 23-Oct-24			
	BS-200	Erect Wall Panels			Erec	
***	BS-220	Erect 2nd floor Structural Steel	15 02-Dec-24			
C (**)	BS-210	Remove Casting Beds	6 02-Dec-24	t 09-Dec-24	Rem	
	BS-230	Prep & Pour 2nd floor	-		£	
-	BS-250	Erect Roof Structural Steel & Deck	17 23-Dec-24	-		
*****	BS-260	Erect Hollw Core Planks			a.i.	
	BS-280	Roof Dry-in			Roof	
	BS-290	Parapet, Flashings & Gutter				
	BS-320	Louvers & Storefront & Windows		-	Louvers	
	BS-300	Exterior Wall Coatings			a (
	BS-310	Railings				
	BS-330					
	BS-340	Exterior Fixtures & Trim			XXenor FXures & IIII	
*****	Interior		146 23-Jan-25	_		
	First Floor	or	-			
	B1-19(B1-190 Fire Rate Structure			Fire Area Structure	
700	B1-10(B1-100 Interior Partitions		-+	e linelini rannon	
	B1-11(B1-110 Overhead M.E.P.F.S. Rough-in				
	B1-180	io Wall Rough			Ma	
in a	B1-12(B1-120 Hang & Finish Drywall	12 06-Mar-25			
	B1-140	.0 Painting				
	B1-160	B1-160 Ceramic Tile	-			
- 1734	B1-130	0 Ceiling Grid & Systems Trim				
	B1-17(B1-170 Systems Trim	-		550	
10.00	B1-15(B1-150 Install Millwork, Doors, & Hardware				
	B1-200	B1-200 Flooring Finishes	14 15-May-25			
*********	B2-21	B2-210 Furnishings & Signage	9 04-Jun-25	`-	Furnshings & Signage	
	Second Floo	Floor				
	B2-18I	B2-180 Access Floor System		-	Acce	
	B2-10/	B2-100 Interior Partitions			Interior Partitions	
******	B2-11(B2-110 Overhead M.E.P.F.S. Rough-in	-+			
	B2-12.	B2-120 Hang & Finish Drywall	-	-		
	B2-14!	B2-140 Painting	6 22-May-25	5 29-May-25		
	Actual Work	Critical Remaining Work			Page 2 of 3 Data Date: 01-Feb-24 TASK filter: All Activities	

				٠,																				0000	
Activity ID		Activity Name	Orig Dur	Start	Finish	401	Mar.	╽┝	2024	1	20	100	YOM		<u>-</u>	Hah Mar	Anr	May	2025	Aug Sep	Nov	Dec	Jan	2026 Feb	Mar
	B2-160	B2-160 Install Ceramic Tile	9	22-May-25	04-Jun-25		nd	May							+		+	4.	<u>=</u>		+	 	ļ		
	B2-130	0 Ceiling Grid & Systems Trim	12	30-May-25	16-Jun-25														Ceiling G	Ceiling Grid & Systems Trim					
	B2-150	10 Install Millwork, Doors, & Hardware	12	17-Jun-25	02-Jul-25														Insta	Install Millwork, Doors, & Hardware	& Hardware				
	B2-170	B2-170 Trimout MEP	2	17-Jun-25	23-Jun-25						••••	••••							Trimout MEP	MEP					
****	B2-190	B2-190 Flooring Finishes	12	17-Jul-25	01-Aug-25	-														Flooring Finishes	hes				
	B2-200	B2-200 Furnishings & Signage	o	04-Aug-25	14-Aug-25															Fųrnishings & Signage	s & Signage				
	Systems		230	10-Dec-24	27-Oct-25																				
	BG-160	Primary Feed U.G.	ဖ	10-Dec-24	17-Dec-24										Primary Feed U.G	d U.G.									
	BG-150	Secondary Power Feed U.G.	4	18-Dec-24	23-Dec-24									I	Secondar	Secondary Power Feed U.G.	U.G.								
	BG-220	Transformer Pad	4	24-Dec-24	27-Dec-24									=	Transformer Pad	ner Pad									
	BG-230	Transformer	4	30-Dec-24	02-Jan-25									<u> </u>	Transformer	rmer									
	BG-170	Primary Feed	9	03-Jan-25	10-Jan-25										Primary Feed	ny Feed									
	BG-100	Install Elevator	35	13-Jan-25	28-Feb-25										Service Servic	Install	Install Elevator								
12.712.7	BG-290	Secondary Feed Wire	80	13-Jan-25	22-Jan-25										.ŭ	Secondary Feed Wire	Wire								
	BG-270	Chillers & Pumps Install	28	31-Mar-25	07-May-25													Chillers & Pr	. 특 -	tall					
,	BG-240	Main Switchger	18	09-Jun-25	02-Jul-25														Main	Main Switchger					
	BG-180	Communication, Life Safety & Data Systems Inter	35	17-Jun-25	04-Aug-25														-	Communicati	Communication, Life Safety & Data Sys	y & Data S	Systems Ir	tems Intergratio	E
	BG-280	Instal HVAC Equipment	24	27~Jun-25	30-Jul-25															■ Instal HVAC Equipment	quipment				
esers.	BG-250	Secondary Feed Terminate & Service	2	03-Jul-25	09-Jul-25														s B	Secondary Feed Terminate & Service	erminate & Se	rvice			
	BG-260	Distribution Panels	12	03-Jul-25	18-Jul-25			-												Distribution Panels					
	BG-120	Terminate Dsitribution	12	21-Jul-25	05-Aug-25															Terminate Dsitribution	sitribution				
	BG-210	HVAC System Integration & Start-up	28	31-Jul-25	08-Sep-25															A.	■ HVAC System Integration & Start-up	tegration &	s Start-up		
******	BG-110	Existing Chiller Tie-in/ Transfer	19	09-Sep-25	22-Sep-25																Existing Chiller Te-in/ Transfer	er Terin/T	ransfer		
	BG-130	T	10	14-0ct-25	27-Oct-25																Gen	Generator			
0	Owner Acceptance	pfance	111	05-Aug-25	06-Jan-26																				
	BG-200	Final Life Safety Inspections	2	05-Aug-25	11-Aug-25															Final Life S	Final Life Safety Inspections	ons:			
	A4040	Systems Commissioning	15	27-Oct-25	17-Nov-25																	Systems	Systems Commissioning	ioning	
	A4000	Final Inspections	2	17-Nov-25	24-Nov-25					:												Final	Final Inspections	- 10 -	
	A4050	Training	r0	17-Nov-25	24-Nov-25						;											Training:	. Б.		
1	A4010	Certificate of Occupancy	-	10-Dec-25	11-Dec-25																	-	Certificate of Occup		ancy
	A4020	Substantial Completion	0 .	11-Dec-25	11-Dec-25																		Substantial Completion	Complet	tion
	A4030	Owner Punchlist	15	11-Dec-25	05-Jan-26																		.∎	Owner Punchlist	hlist
	A4060	Close-out	15	11-Dec-25	05-Jan-26																			Close-out	
	A4070	Final Completion	-	05-Jan-26	06-Jan-26																		Fina	Final Completion	etion
		I.								Page 3 of 3	, e		9			Data Date	Data Date: 01-Feb-24	14 Hies							
	Remaining work	ork 🔶 🔶 ivillestone																							

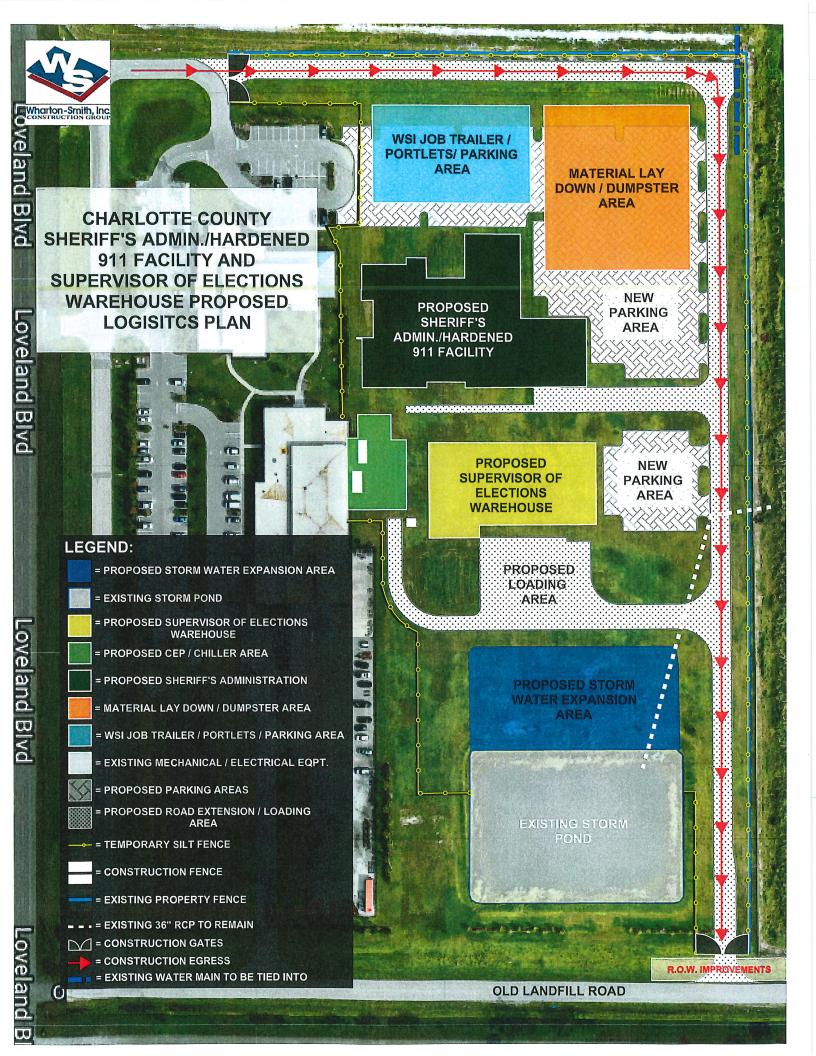

GUARANTEED MAXIMUM PRICE

Charlotte County

Sheriff's Administration/Hardened 911 Facility

GMP PACKAGE

